

SIS Modernization Update

LSU Workday Student Website

www.lsu.edu/workdaystudent

The screenshot shows the homepage of the LSU Workday Student website. At the top, there is a dark purple navigation bar with the LSU logo and 'WORKDAY STUDENT' on the left, and links for 'MYLSU', 'CAMPUS CRIME STATS', 'GIVE', 'APPLY', 'VISIT', and a 'SEARCH' button on the right. Below this is a secondary navigation bar with links for 'About Us', 'Academics', 'Admissions & Aid', 'Athletics', 'Student Resources', 'Research & Industry', and 'LSU Online'. A breadcrumb trail shows 'Home / Workday Student'. The main content area features a large banner with a background image of trees and the text 'WORKDAY STUDENT' in white, with a yellow horizontal bar above it. Below the banner is a dark purple navigation bar with links for 'ABOUT', 'TIMELINE', 'UPDATES', 'TRAINING', 'TEAM', and 'FAQS'. The main heading is 'About Workday Student', followed by a paragraph stating that LSU has selected Workday Student as the vendor for its new, modernized student information system, which will be implemented across LSU A&M, LSU of Alexandria, LSU Eunice, and LSU Shreveport. A second paragraph explains that the project will have a significant impact on the way students, faculty, and staff work, study, and navigate collegiate life, and that full transparency will be maintained throughout the implementation.

LSU WORKDAY STUDENT

MYLSU CAMPUS CRIME STATS GIVE APPLY VISIT

[About Us](#) [Academics](#) [Admissions & Aid](#) [Athletics](#) [Student Resources](#) [Research & Industry](#) [LSU Online](#)

Home / Workday Student

WORKDAY STUDENT

[ABOUT](#) [TIMELINE](#) [UPDATES](#) [TRAINING](#) [TEAM](#) [FAQS](#)

About Workday Student

LSU has selected Workday Student as the vendor for its new, modernized student information system. LSU A&M, LSU of Alexandria, LSU Eunice, and LSU Shreveport are working together on this project to achieve a unified student information system across these institutions.

We know that this project will have a significant impact on the way our students, faculty, and staff work, study, and navigate collegiate life. As such, we pledge full transparency throughout the next several years of implementation, and we strive to keep all constituents of each participating institution updated and involved.


Timeline & Accomplishments

LSU Student Timeline

(59)

Customer Prep Plan Continued Engagement Architect & Configure (Worksets) Test Deploy (MTP1, MTP2) Business Function Milestones (M1 - M5)

We are here

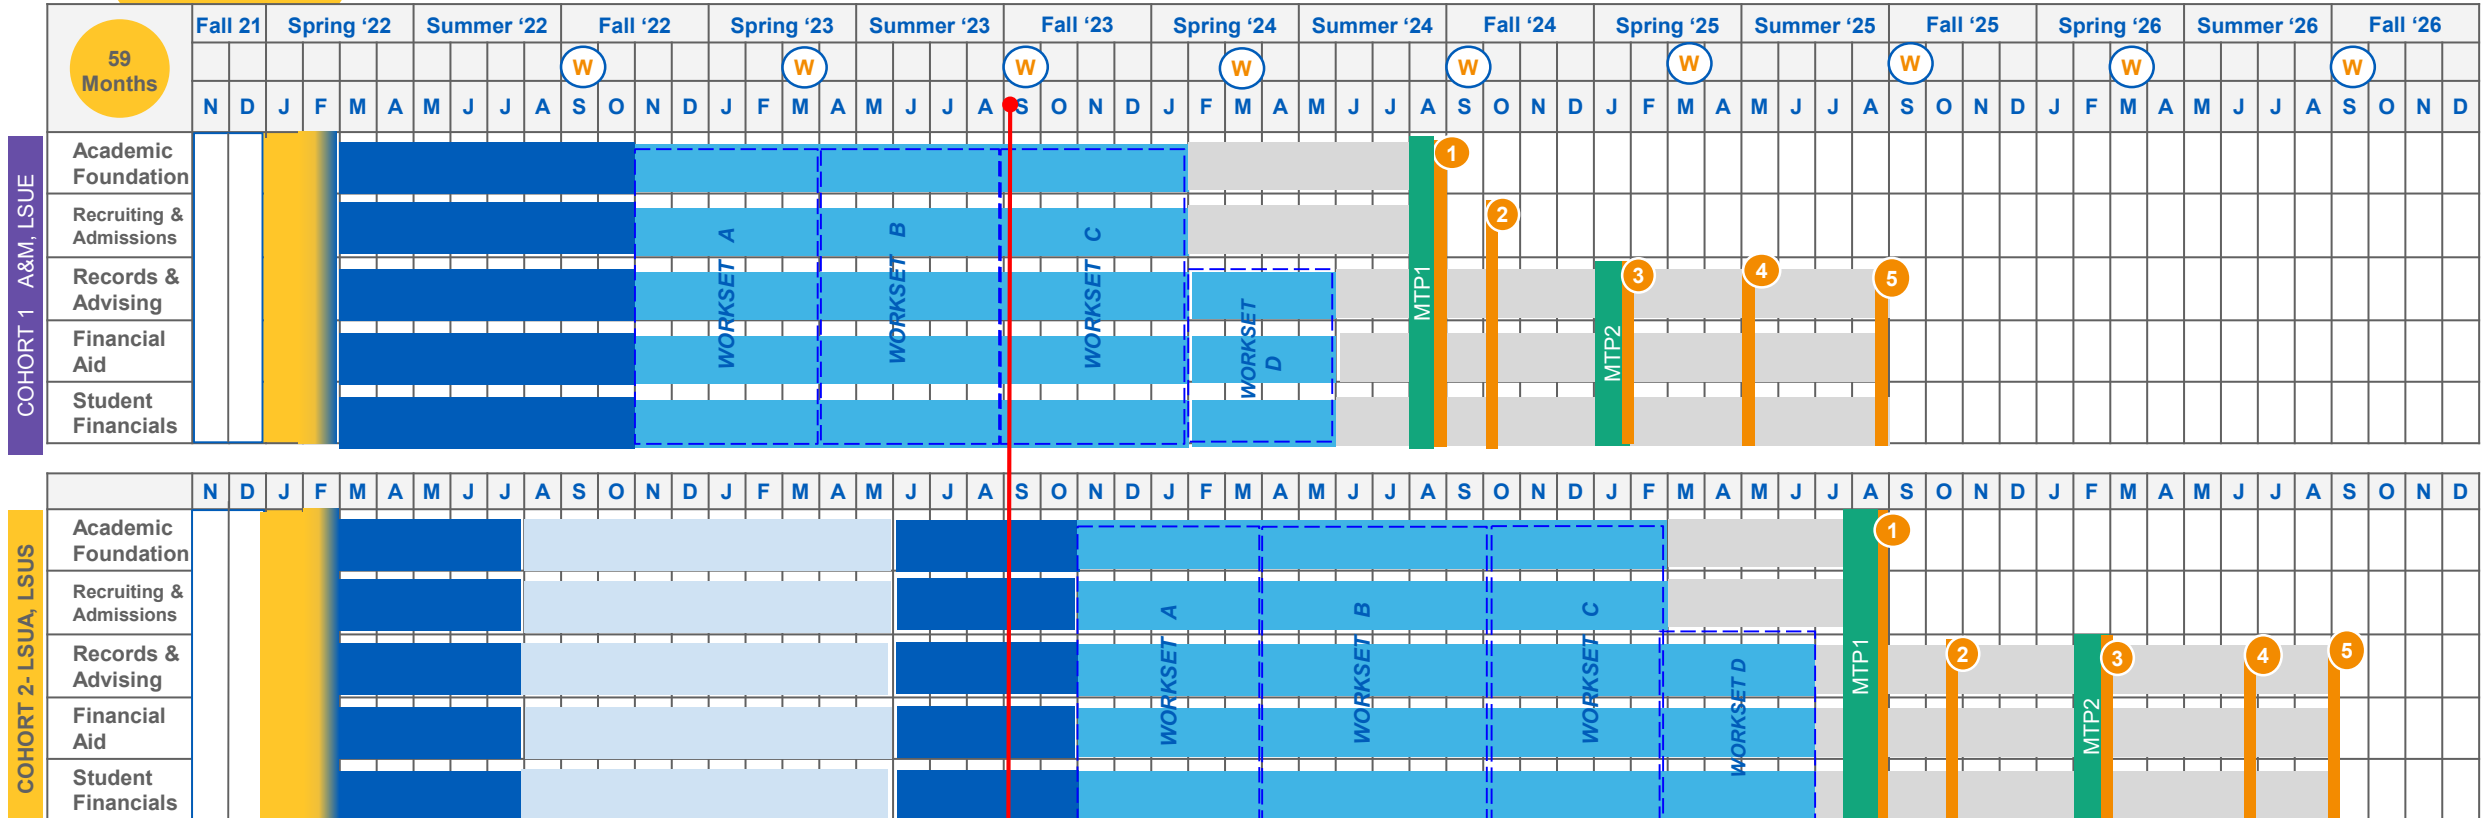

- Onsite
- ① plan
- ② a&c
- ③ a&c
- ④ plan
- ⑤ a&c
- ⑥ plan
- ⑦ test
- ⑧ a&c
- ⑨ test
- ⑩ deploy
- ⑪ a&c
- ⑫ test
- 13a deploy
- 14 test
- 13b deploy
- 15 test
- 16 test
- 17 deploy
- 18 test
- 19 deploy
- 20 test
- 21 test

- ①

 - Recruiting & Admissions
 - Application Fees & Tuition Deposits
 - Academic Units & Levels
 - Student Core
 - Program of Study Profiles
 - Calendars
 - Educational Institutions
 - Course Catalog
 - Class Schedule
- ②

 - Verifications, Awarding & Packaging for New Students
 - ISIRs
 - Course Catalog (Cohort 2 Only)
 - Class Schedule (Cohort 2 Only)
- ③

 - Registration & Advising
 - Student Conversion (All)
 - Verifications, Awarding & Packaging for Continuing Students
 - Fee Calculations, Sponsors, & Waivers
 - Payment Plans
- ④

 - Payments
 - Cashiering Integration
 - Payment Plans
 - Disbursement
 - R2T4
 - Class Schedule (LSUE)
- ⑤

 - Payments
 - Cashiering Integration
 - Disbursement
 - R2T4
- ⑥

 - Student Financials Balances
 - Grading
 - Graduation
 - Transcript Generation
 - End-of-term Processing

LSU A&M Only
 • Student Financials Balances
 • Grading
 • Graduation
 • Transcript Generation
 • End-of-term Processing

Summer is Financial Aid Header for A&M
 Summer is Financial Aid Trailer for LSUE, LSUA, LSUS

LSU Cohort 1 Architect and Configuration (A&C) Stage Overview


A&C Stage

November 2022 - March 2023


April 2023 - August 2023

September 2023 - January 2024

February 2024 - May 2024

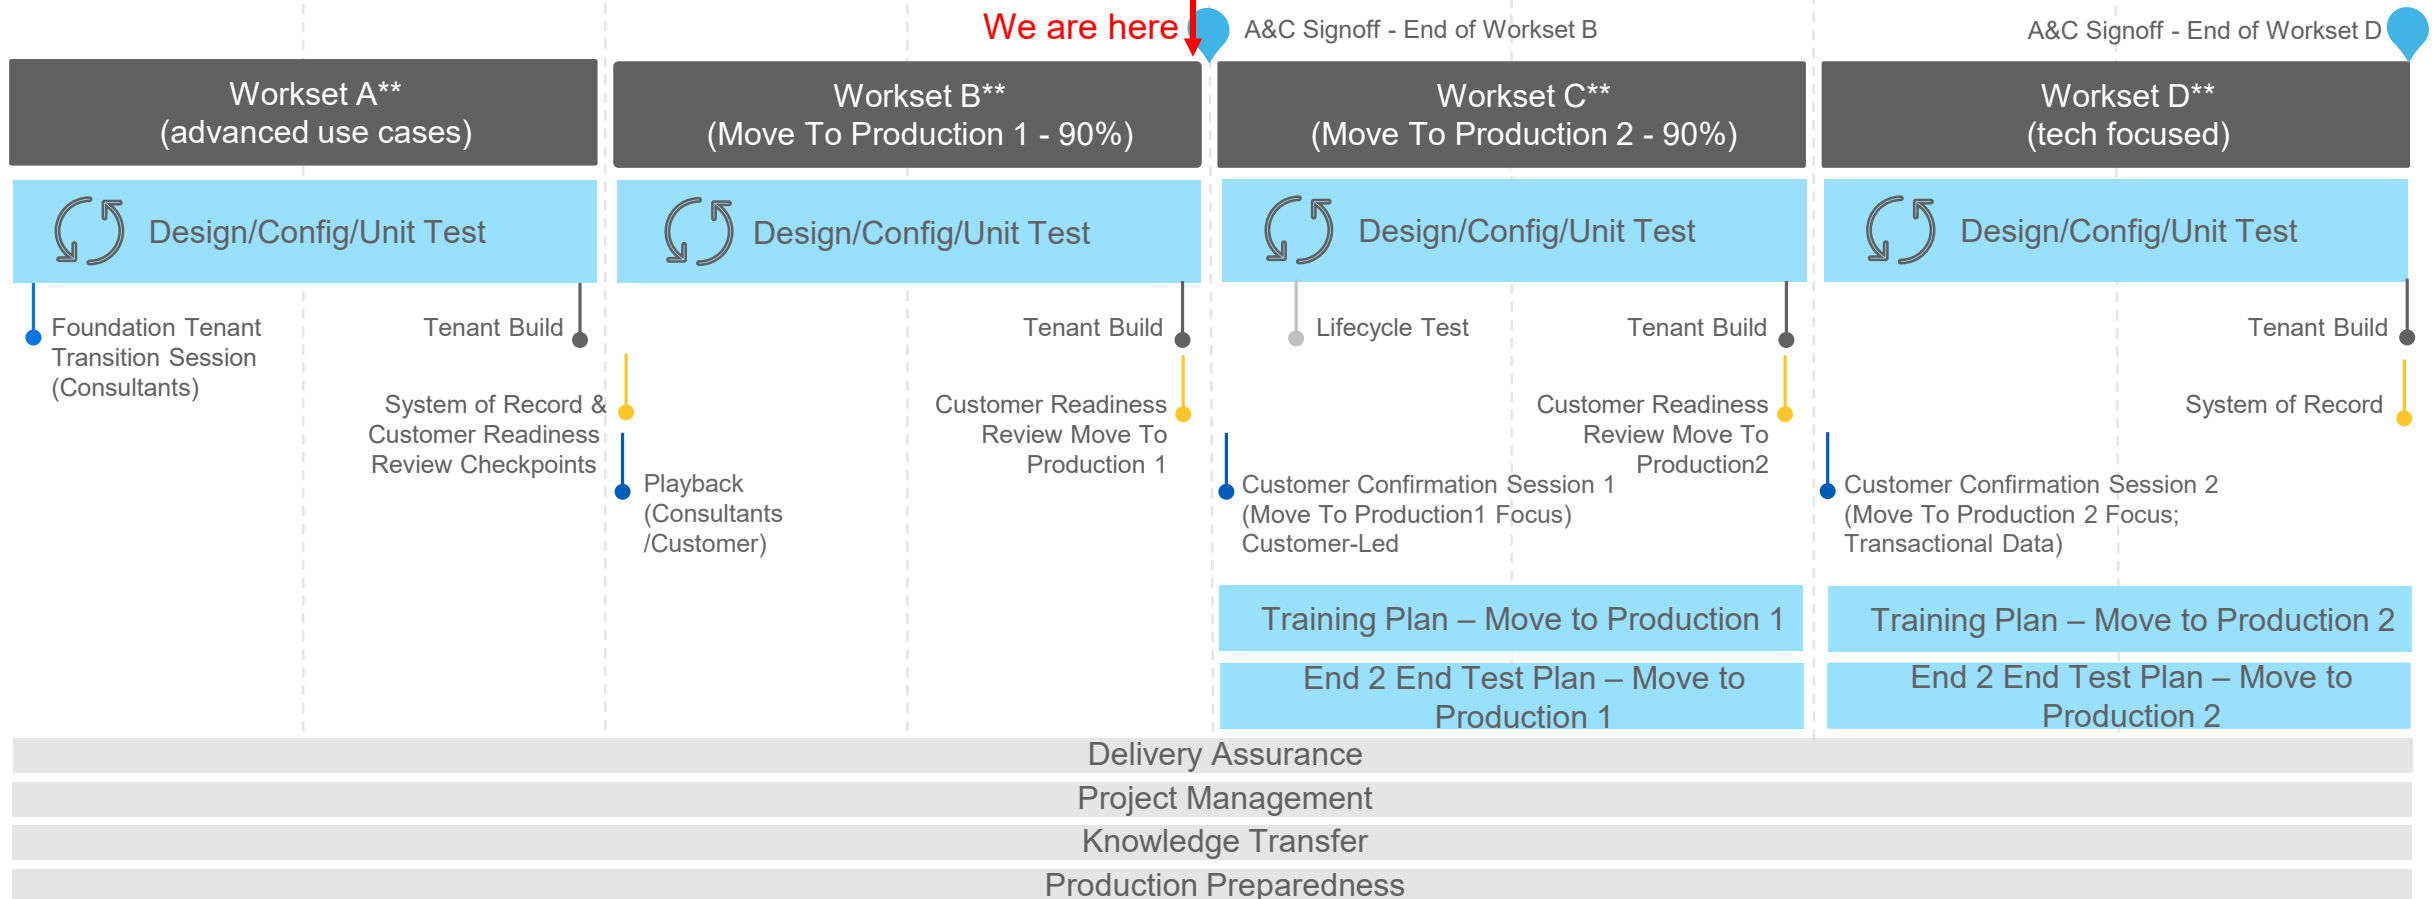

LSU Cohort 2 Stage Details

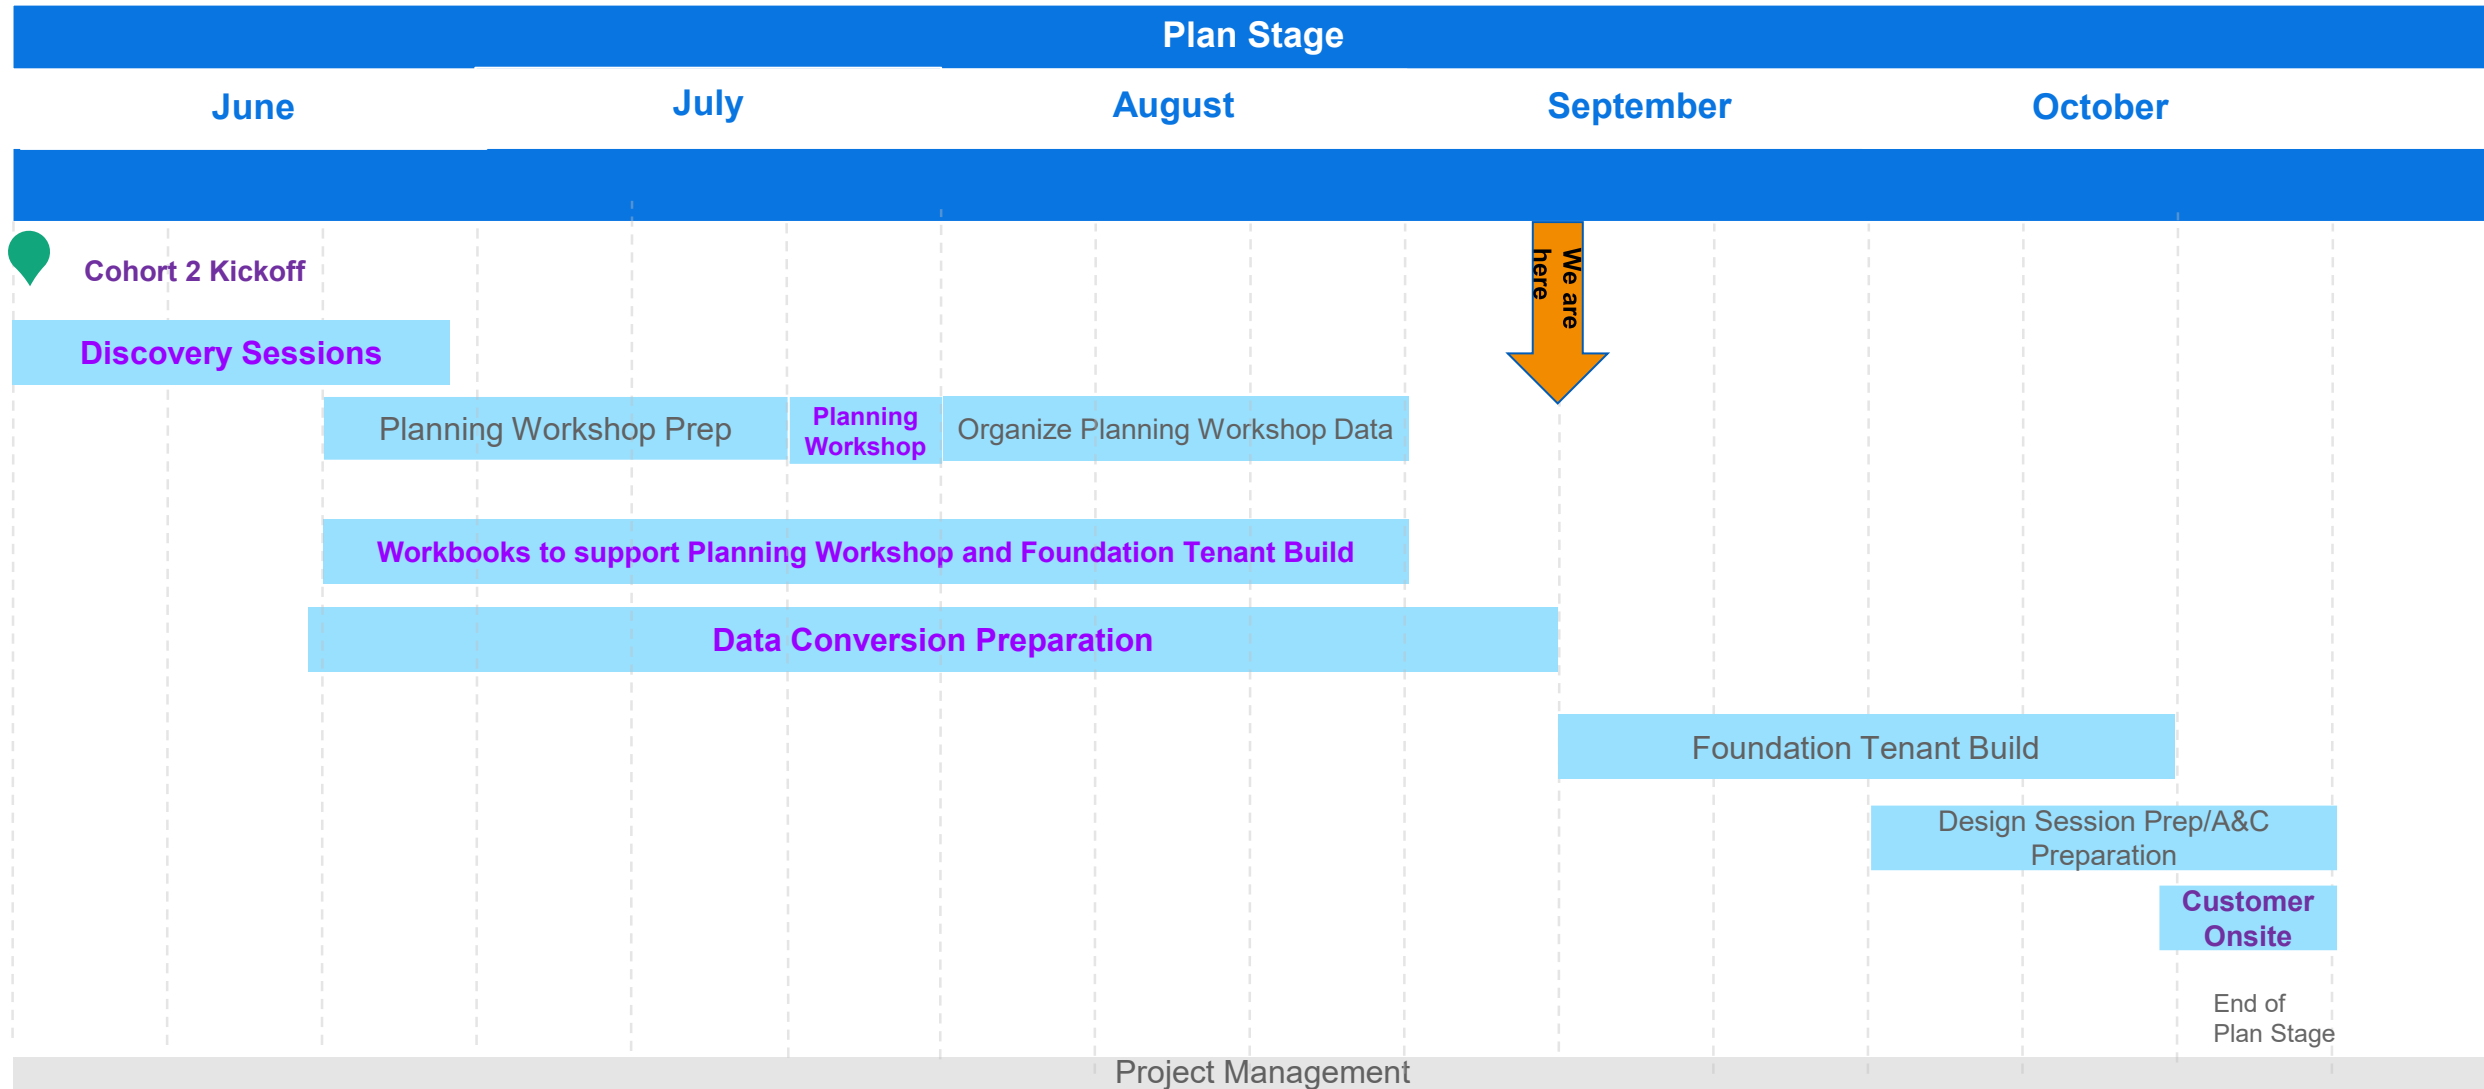

Key Accomplishments & Activities

as of 8/1/2023

Item	Due Date	Owner	Description/Update	Status
Cohort 2 Discovery Sessions	6/30/2023	Workday , LSU	Multiple sessions to validate current business processes	Complete
Cohort 2 Planning Workshop	7/27/2023	Workday , LSU	Onsite sessions to validate timeline, plan workset objectives, integrations and data conversions and review system of record	Complete
Training Phase III – Spring 2023	NA	LSU	Phase III Spring training underway	In progress
Cohort 1 Architect and Configuration (A&C) Workset B Objectives	8/31/2023	Workday , LSU	Completion of Workset Objectives, Data Conversion Programs and Integration Requirements identified for Workset B	In progress
Cohort 1 Workset B Tenant Planning and Build	9/29/2023	Workday	Build tenant based on Workset B Design and Configuration to be utilized for Workset C	In progress
Cohort 2 Foundation Tenant Planning and Build	10/13/2023	Workday	Build Cohort 2 Foundation Tenant to support Workset A Design and Configuration activities	In progress
Cohort 1 Workset C Tenant Validation	10/6/2023	Workday , LSU	Validate tenant build for Cohort 1 Workset C	Not Started

Training Updates

Key Training Dates





- **SEPTEMBER 2023**
 - Onboard Deloitte Training Developers
 - Begin to draft curriculum
- **MARCH 2024**
 - Finalize the Train-the-Trainer program and end-user training delivery
- **APRIL 2024**
 - Begin Train-the-trainer program(s)
 - End user training delivery begins
- **MAY 2024 – JANUARY 2025**
 - End user training delivery on-going
 - Development of training materials based on the on-going milestones

Student Program Update



Student Program Summary

as of 8/1/2023

Project	Due Date	Institution	Owner	Update	% Complete	Status	Health
Workday Student	Dec 2026	All	University Administration	59% complete with all target objectives for the Workset, planning workshop for Cohort 2 was July 25-27	21%	In Progress	
Data Warehouse	Dec 2026	All	Data Governance	Working to build integrations to feed Workday data to the data warehouse, upon completion re-platforming existing reports will start	32%	In Progress	
Cashiering	Jun 2025 Cohort 1 Aug 2025 Cohort 2	All	Accounting Services	Implementation meeting cadence established to begin in September. Coordinating timeline needed for Workday Student.	12%	In Progress	
Identity & Access Management	2024	LSUAM	IT Security & Policy	Okta has been selected as a replacement to manage digital identities and control user access to information	3%	In Progress	
Form 1042-S Reporting	Dec 2025	LSUAM	Accounting Services	No new updates, slated to start in Dec 2025	0%	Not Started	
Identity & Access Management	TBD	LSUS	ITS	No new updates	0%	Not Started	

Projects with Resource Cross-over

as of 8/1/2023

EAB Navigate	TBD	LSUE	ITS	Going live in the Fall with currently planned functionality	100%	Complete	
Legacy System Decommissioning	Dec 2025	LSUAM	ITS	Replace and decommission legacy SIS	0%	Not Started	
Legacy System Decommissioning	TBD	LSUA	ITS	Replace and decommission legacy SIS	0%	Not Started	
Legacy System Decommissioning	TBD	LSUE	ITS	Replace and decommission legacy SIS	0%	Not Started	
Legacy System Decommissioning	TBD	LSUS	ITS	Replace and decommission legacy SIS	0%	Not Started	
